

Photo by Kelley Ellis

Construction

Progressing



We are 84% complete in constructing the Tribal Center. Schedule "B", the community center completion, has been extended to May 3, 1983 due to adverse weather conditions experienced during winter months. Schedule "S", water, sewer and parking lot, will also be extended for completion by July 15, 1983. Bureau of Indian Affairs, Branch of Roads, construction will begin about May 15, 1983 and completion date is anticipated for June 30. As of March 31, 1983, the building is in the finish tages; eg— painting, tile work, finish hardware, food service and floor covering. The basketball backboard and hoop have been installed . . . one more month and the building will be ready for occupancy except the road and parking lot will not be completed until the end of June. All construction will be finished in time for the annual Pow Wow held later in August.

Any additional information, please contact Dale Hile or Marcella Butler at (503) 444-2533.



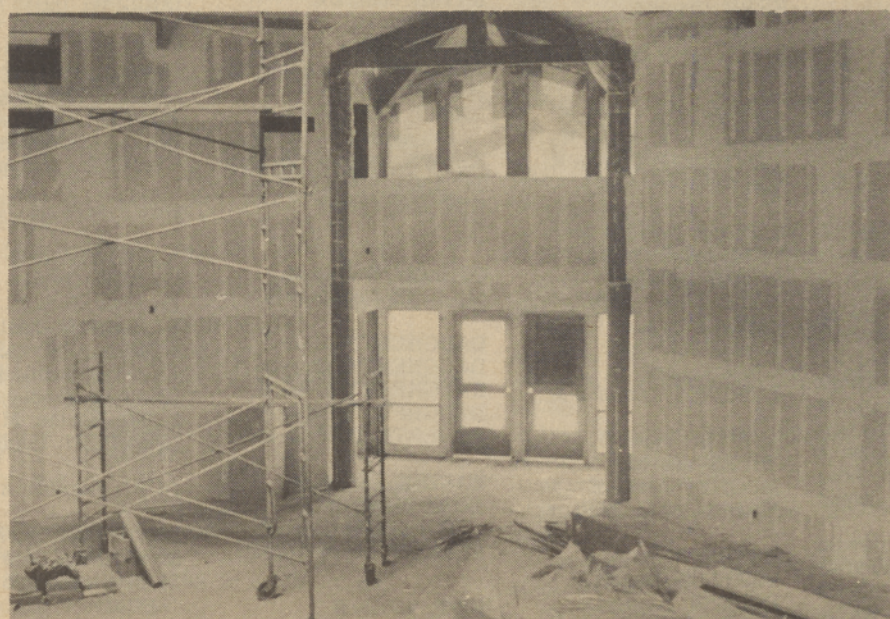


Photo by Kelley Ellis

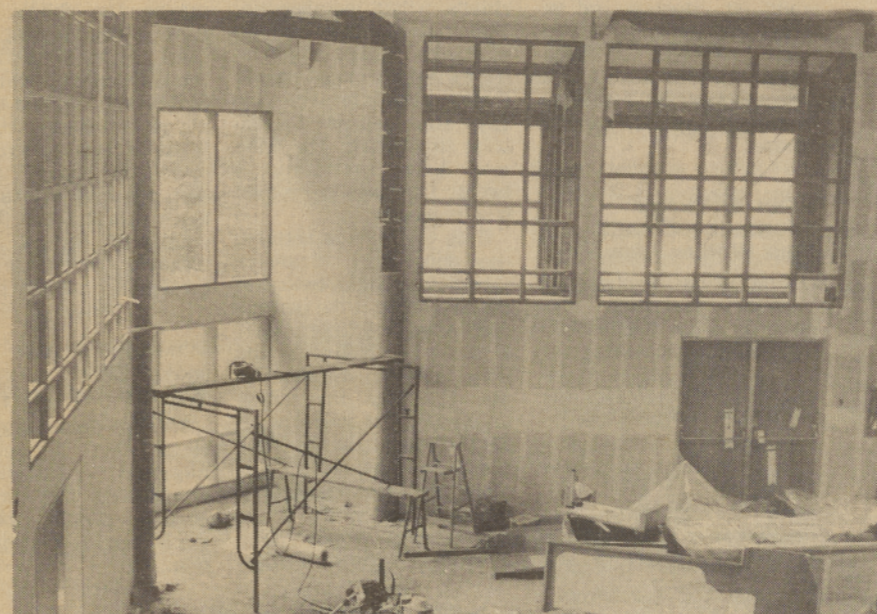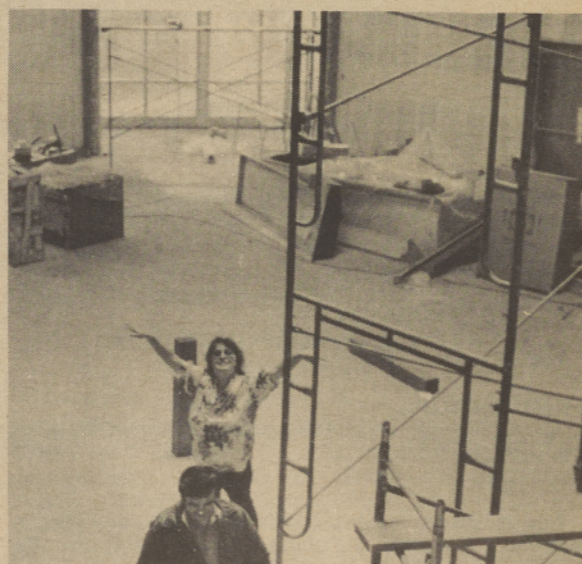

On Tribal Center



Photo by Kelley Ellis

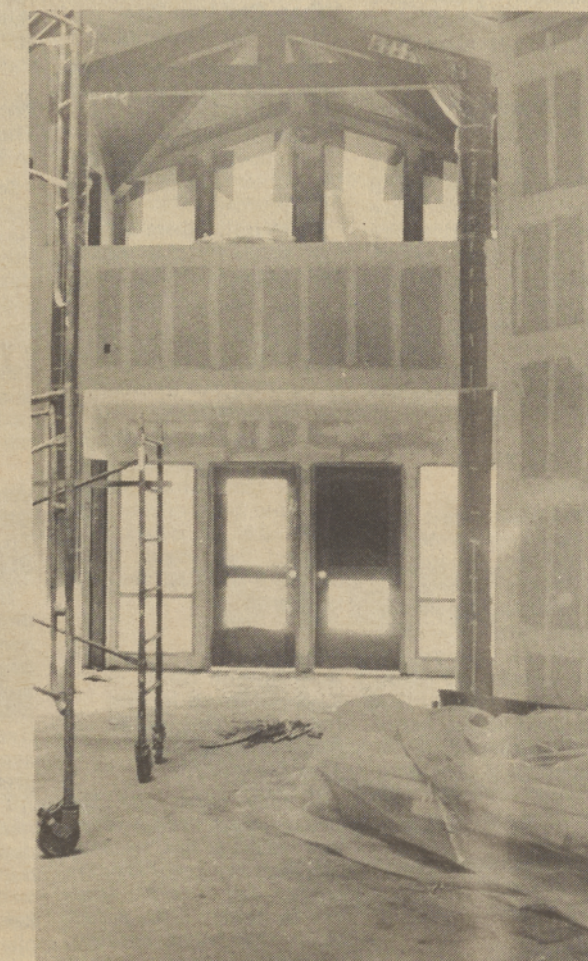
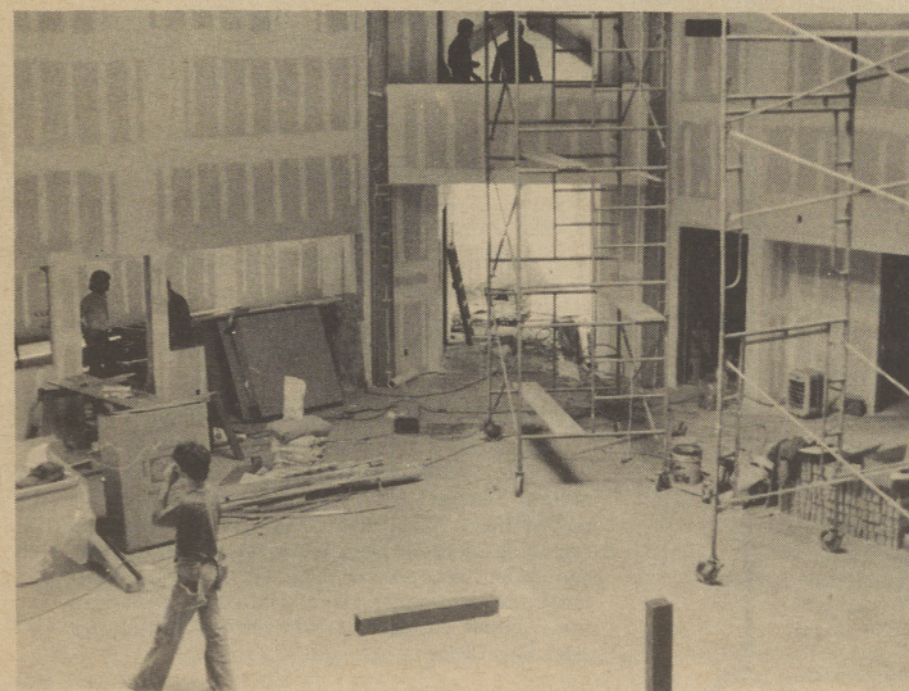
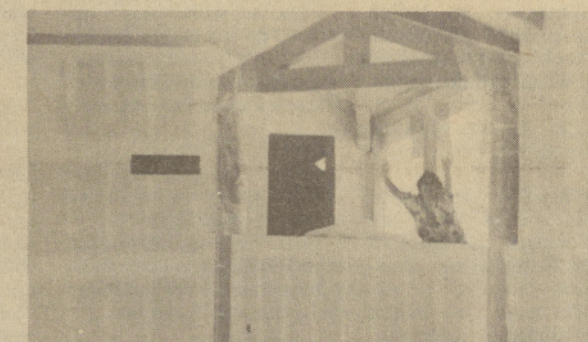


Photo by Kelley Ellis
